Delivery 1 - Load 1 of 2 - Artic 13.6 m

10 pallets in 5 of 5 floor positions | 241 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

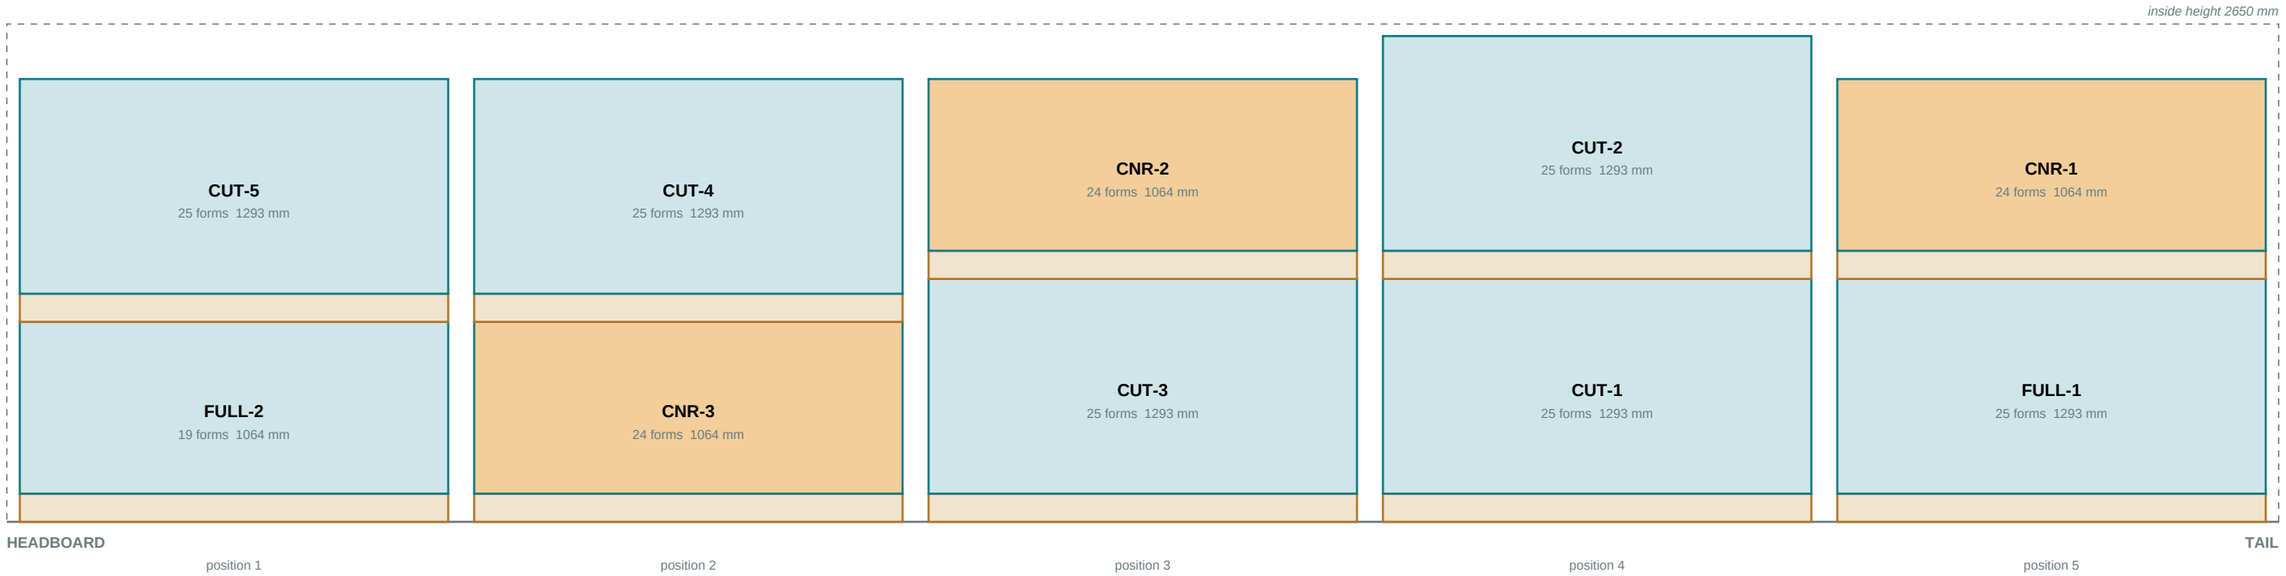

Unload order - 9 of 9 pallets come off out of build order, the price of stacking tallest forward

1. CNR-1 6in XR35 corners 24 forms courses L1 courses 1-2
2. FULL-1 6in XR35 straights 25 forms courses L1 courses 1-4
3. CUT-2 6in XR35 straights 25 forms courses L1 courses 1, 2, 3, 4, 5, 7, 10
4. CUT-1 6in XR35 straights 25 forms courses L1 courses 1, 2, 3, 4, 5, 6, 7, 8, 9, 10, 12
5. CNR-2 6in XR35 corners 24 forms courses L1 courses 2-4
6. CUT-3 6in XR35 straights 25 forms courses L1 courses 2, 3, 4, 5, 6, 8, 9, 10, 11
7. CUT-4 6in XR35 straights 25 forms courses L1 courses 3, 4, 5, 6, 7, 9, 10, 11
8. CNR-3 6in XR35 corners 24 forms courses L1 courses 4-6
9. CUT-5 6in XR35 straights 25 forms courses L1 courses 4, 5, 6, 7, 8, 12
10. FULL-2 6in XR35 straights 19 forms courses L1 courses 5-10

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-090 Insubloc - Tyn Y Bonau Road, Pont…	FORMS	241
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	10	TALLEST	2586 mm

Delivery 1 - Load 2 of 2 - Artic 13.6 m

2 pallets in 1 of 5 floor positions | 33 forms | tallest column 1900 mm of 2650 mm inside height

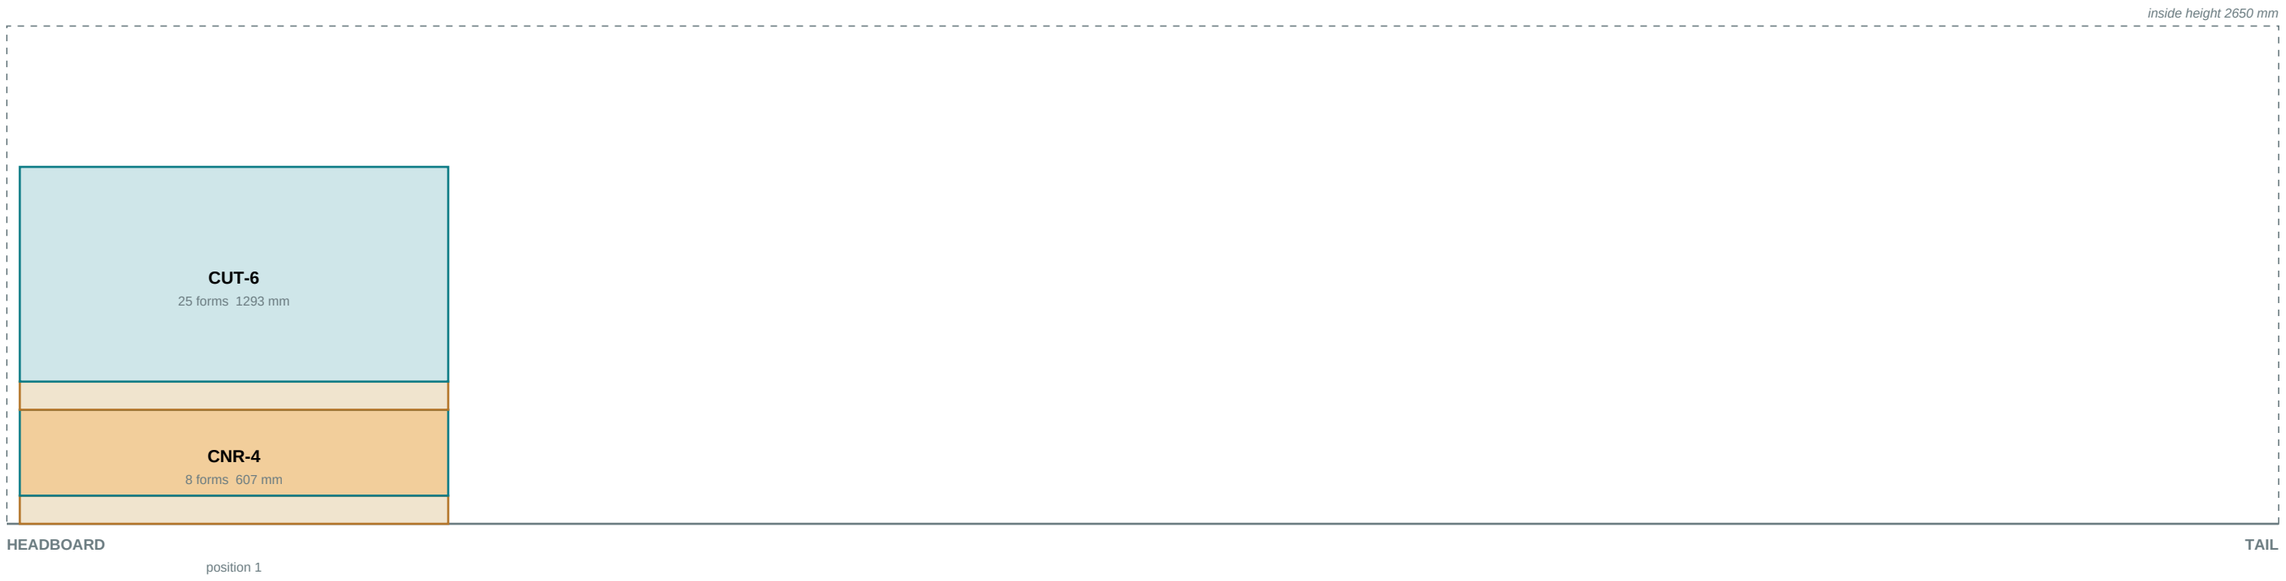

Unload order - 1 of 1 pallets come off out of build order, the price of stacking tallest forward

1. CUT-6 6in XR35 straights 25 forms courses L1 courses 5, 6, 7, 8, 9, 11, 12
2. CNR-4 6in XR35 corners 8 forms courses L1 course 6

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 2**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-090 Insubloc - Tyn Y Bonau Road, Pont…	FORMS	33
VEHICLE	Artic 13.6 m	POSITIONS	1 of 5
PALLETS	2	TALLEST	1900 mm
